

School Board Update New Fredericksburg MS

June 6, 2022



TIMELINE

PROGRESS

March 28

Interim Agreement

April 21

WGMS Faculty Meeting

April 28

TRC Meeting

April 29

Steering Committee Meeting

May 5

Steering Committee Meeting

May 9

WGMS User Meeting #1

May 11

WGMS User Meeting #2

May 12

Community Meeting #1

May 18

Community Meeting #2


June 3

35% Documents to English for Pricing

June 6

School Board Update

SITEPLAN

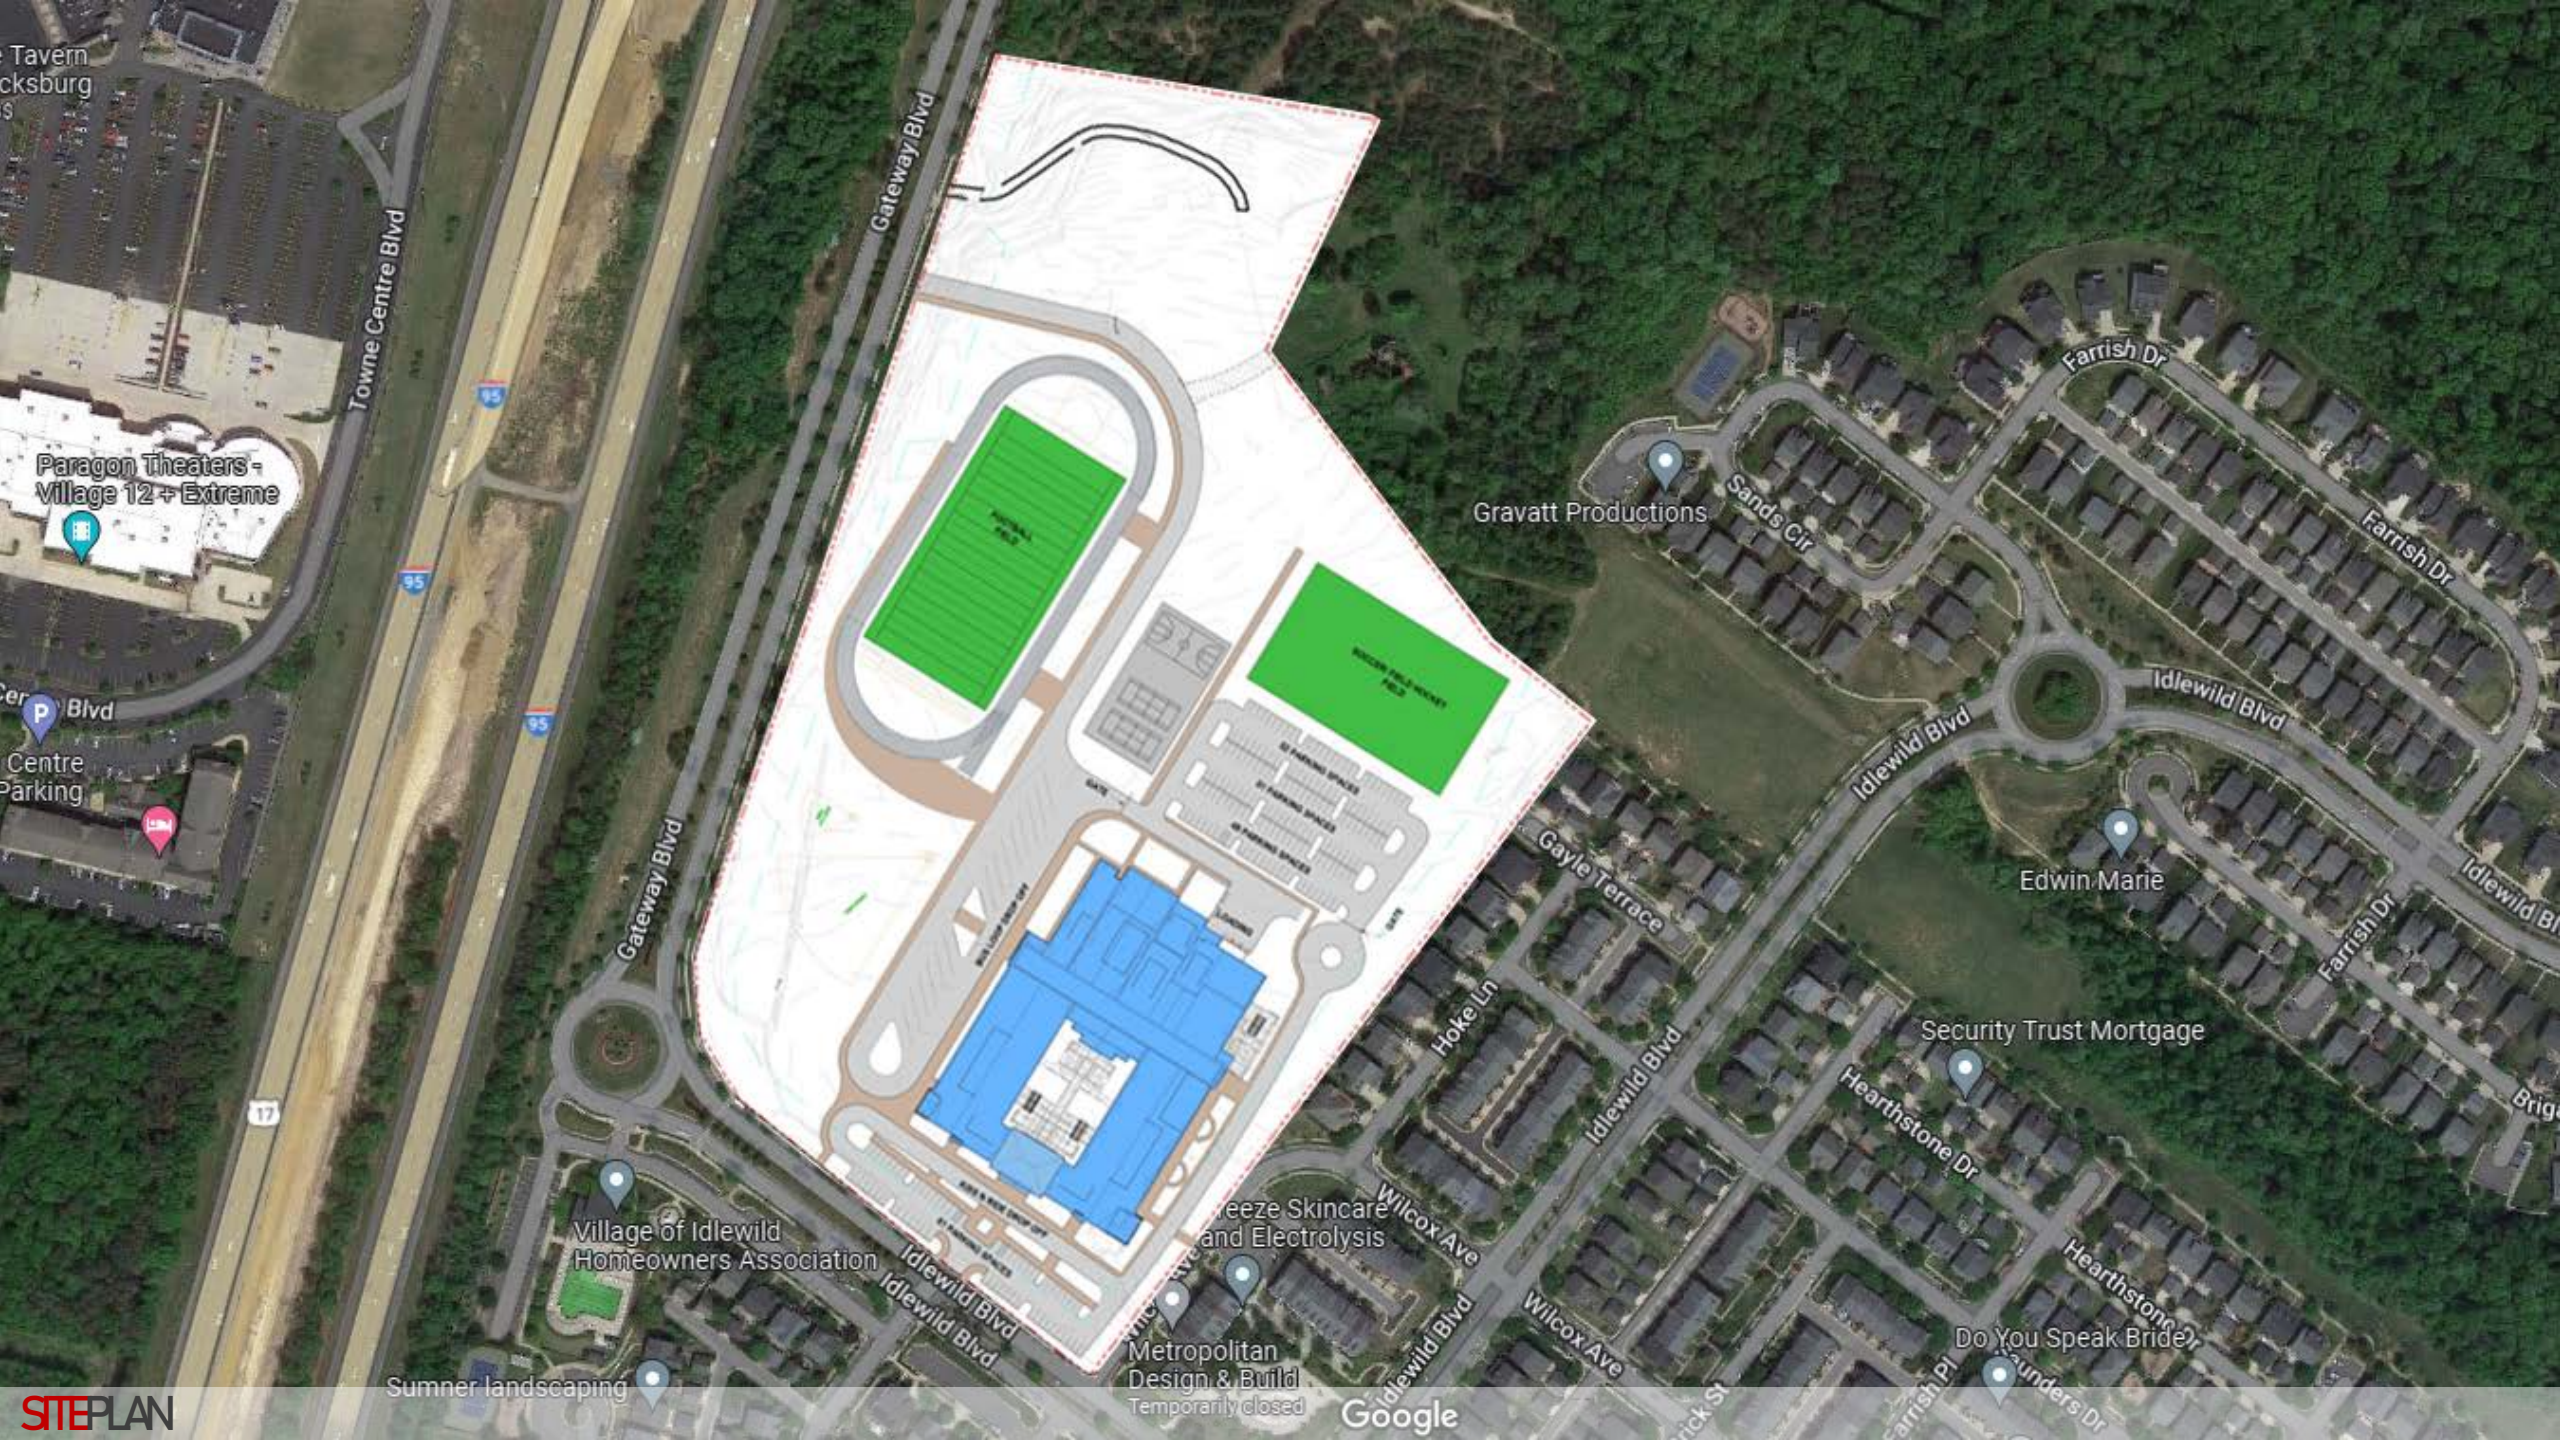

Tavern
cksburg

Paragon Theaters -
Village 12 + Extreme

Centre
Parking

Towne Centre Blvd

Gateway Blvd

Gateway Blvd

Sumner landscaping

Village of Idlewild
Homeowners Association

Metropolitan
Design & Build
Temporarily closed

Google

Gravatt Productions

Sands Cir

Farrish Dr

Farrish Dr

Edwin Marie

Security Trust Mortgage

Hearthstone Dr

Do You Speak Bride?

Hearthstone Dr

saunders Dr

Hoke Ln

Gayle Terrace

Wilcox Ave

Wilcox Ave

Trick St

Farrish Pl

Brig

Idlewild Blvd

Idlewild Blvd

Idlewild Blvd

Idlewild Blvd

Idlewild Blvd

Idlewild Blvd

95

95


95

17

FLOORPLANS



FIRST FLOOR

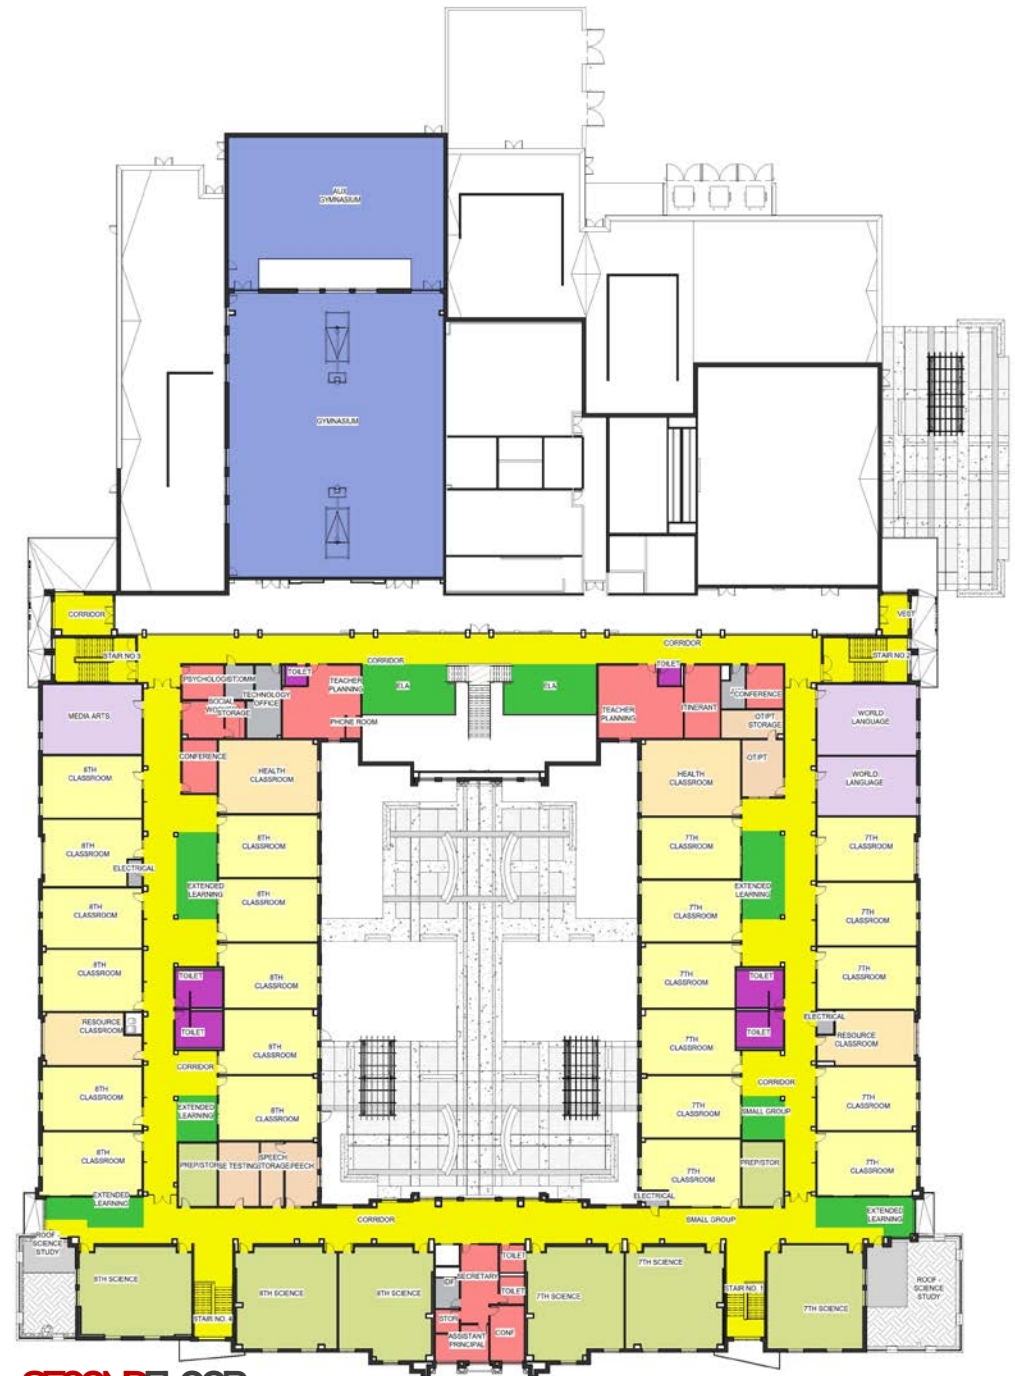

SECOND FLOOR

- LEGEND
- Administration
 - Athletics
 - Circulation
 - Classroom
 - Classroom - Specialty
 - Extended Learning
 - Science
 - Special Education
 - Support / MEP / Stor
 - Toilets
 - Woodstair

NEXTSTEPS

NEXT STEPS

June	35% Pricing Prepared
July 1	35% Documents Delivered to FCPS/City
July	Review Documents Adjust Project Scope (if necessary) Prepare Comprehensive Agreement
August	Public Hearing Execute Comprehensive Agreement
